

Village of Dolgeville Engineer's Monthly Update

November 2022

Active Projects


Planning Board – Caufield Development SEQR

- **The Village Board should complete the SEQR process at this Board meeting.**

Beaver Brook Floodplain Study / LOMR

- Waiting on the final review of the proposed LOMR by FEMA.
- The estimated project timeline prepared by FEMA's consultant is shown below for the record.

Estimated Project Timeline:

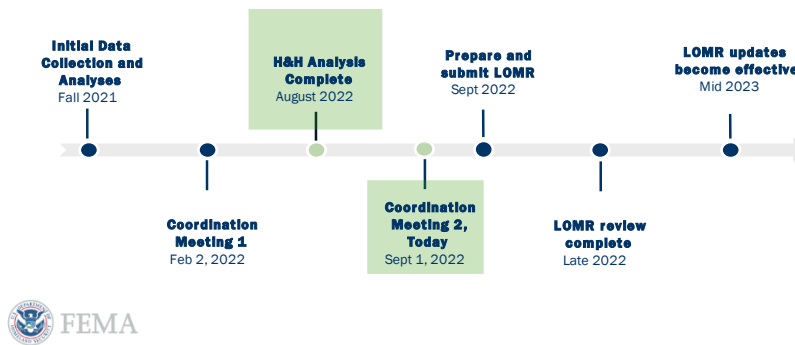

Main Street Sewer Replacement Project

- Design work is continuing throughout the winter with bid documents anticipated in early 2023.
- Needs to be coordinated with the FEMA Projects (Fink Creek) and NYSDOT Projects (Beaver Brook) as we continue to move forward. We have a meeting set with NYSDOT on 12/1/2022.

Congressionally Directed Funding Applications (no change)

- Awaiting news regarding the award of these projects.

Halloween Flood Event (404 Mitigation Program) DR4472

- **A single bid was received on 11/16 for the appraisal services needed for the project and should be awarded at this Board meeting.**
- **We have a proposal for the hazardous material survey ready for Board approval. (B&L)**
- Key dates for the project:
 - o the project must be completed by June 17, 2024.
 - o a property must be demolished, removed, and the site restored within 90 days of the acquisition of the property by the Village.

EPA Lead and Copper Rule Changes (no change)

- The Village will need to provide an inventory to all service lines to the local DOH by October 16, 2024.
- The Village submitted a grant application for assistance with completing the LSL Inventory on August 31, 2022.

Halloween Flood Event (FEMA)

- The most recent updates from FEMA are below:
 - o PN130882 - Emergency Protective Measures – This project has been completed.
 - o PN130884 - Fink Storm Water Drainage System – Landowner agreements for construction continue to be the final item remaining before this project can be obligated.

Village of Dolgeville Engineer's Monthly Update

November 2022

- PN130885 - North Main Street Sewer, Water Distribution and Storm Drainage Reconstruction – We are still working on the active RFI with DHSES and FEMA for this project. Once obligated, this project will be incorporated into the existing Main Street Sewer Replacement Contract.
- PN130886 - North Main Street Roadway Reconstruction – This project has been obligated.
- PN130890 - Village Wide Debris Removal – This project has been completed.
- PN153162 - Management Costs – Pending for the obligation or withdrawal of all the projects to be sent to the CRC.
- DHSES is requesting that the Village to continue to prepare the back-up paperwork required for PN153162 - Management Costs.

NYS Parks Grant

- Final design of this project was submitted to NYS Parks for their approval.

NY Forward Grant

- The application to this program was submitted on September 23, 2022. With short notice, the Village team and Saratoga Associates prepared a presentation which was given on October 24, 2022 at Herkimer County Community College to the Regional Economic Development Council and staff from the Department of State.
- Awards are anticipated before the end of the year.

Sanitary Sewer Collection System Investigation, Phase I

- Working with Michele and Amy over the past month to develop the reimbursement request for this project.

Sanitary Sewer Collection System Investigation, Phase II (EPG #105559) (no change)

- Report preparation by the Consultant Team (B&L) is continuing for this project.

WWTP Concrete Deterioration Repairs

- Replacement of the stairs has been completed along with repair / restoration of the eastern primary tank wall.
- A change order for additional work in restoring a portion of the western primary tank wall was approved at a special meeting on 11/16. Work included in this change order is already being prepared and should be completed within the next two weeks.

WTP Spillway Failure Repairs

- I completed and submitted the NYSDEC / ACOE Joint Permit Application for this project on May 19, 2022.
- We have received a permit from the NYSDEC and confirmation that the project falls under the Nationwide Permit from ACOE.
- This project should be bid in late winter for construction in Spring 2023.

Village Water Tower and Industrial Park Utilities

- Amy, Neal, and I have continued to coordinate information related to water and sewer systems with the IDA's Consultant Team throughout the past month.

ACOE Study of the East Canada Creek

- Attended a meeting with ACOE and NYSDOT to discuss the status of the East Canada Creek study.
- Currently collecting information related to the recent ice jam for ACOE.

DPW Project List

- Repair / replacement of 4 major creek culverts throughout Village
- Vehicle acquisition / replacement
- Co-funding sources for Main Street Paving / ADA Compliance Project
- DPW Garage Construction Grants
- Greenway Extension Grants (Main Street to Gehring Tricot)
- Beaver Brook and Thresher Brook Floodplain, FEMA

Village of Dolgeville Engineer's Monthly Update

November 2022

- Army Corps of Engineers, East Canada Creek (*no change*)
- 2nd Street Drainage Improvements (*on hold*)
- DEC Mohawk River Watershed Grants – Round 5 (On hold pending 404 Program @ North Main Street)

WTP / Water Distribution System Project List

- Siding Repairs at Rear of WTP
- Grant Funded Study / Hydraulic Model in 2022/2023
- Water Operator's License
- Water Transmission Main Mapping / Grants
- GIGP Water Meter Resubmittal (w/ B&L)
- NYSDOH Disinfection Byproducts (*on hold*)

WWTP / Collection System Project List

- Phosphorous Removal Limits Changing, 1.0 (EPG)
- Incorporate 2019 Video/Condition Assessment Into GIS / HOCCPP System
- Main Street Sanitary Sewer Project / Financing, EFC

Future ARPA Project List

- Primary Tank Concrete Repairs
- WTP Disinfection Byproducts
- WTP and WWTP Preliminary Engineering Reports
- Collection System Repairs

Creeks and Flood Prevention

- East Canada Creek Sediment / Hydraulics; Dam Removal (Weston and Sampson)
- Van Buren Street Ice Jam / Flooding; ACOE Design and Permitting
